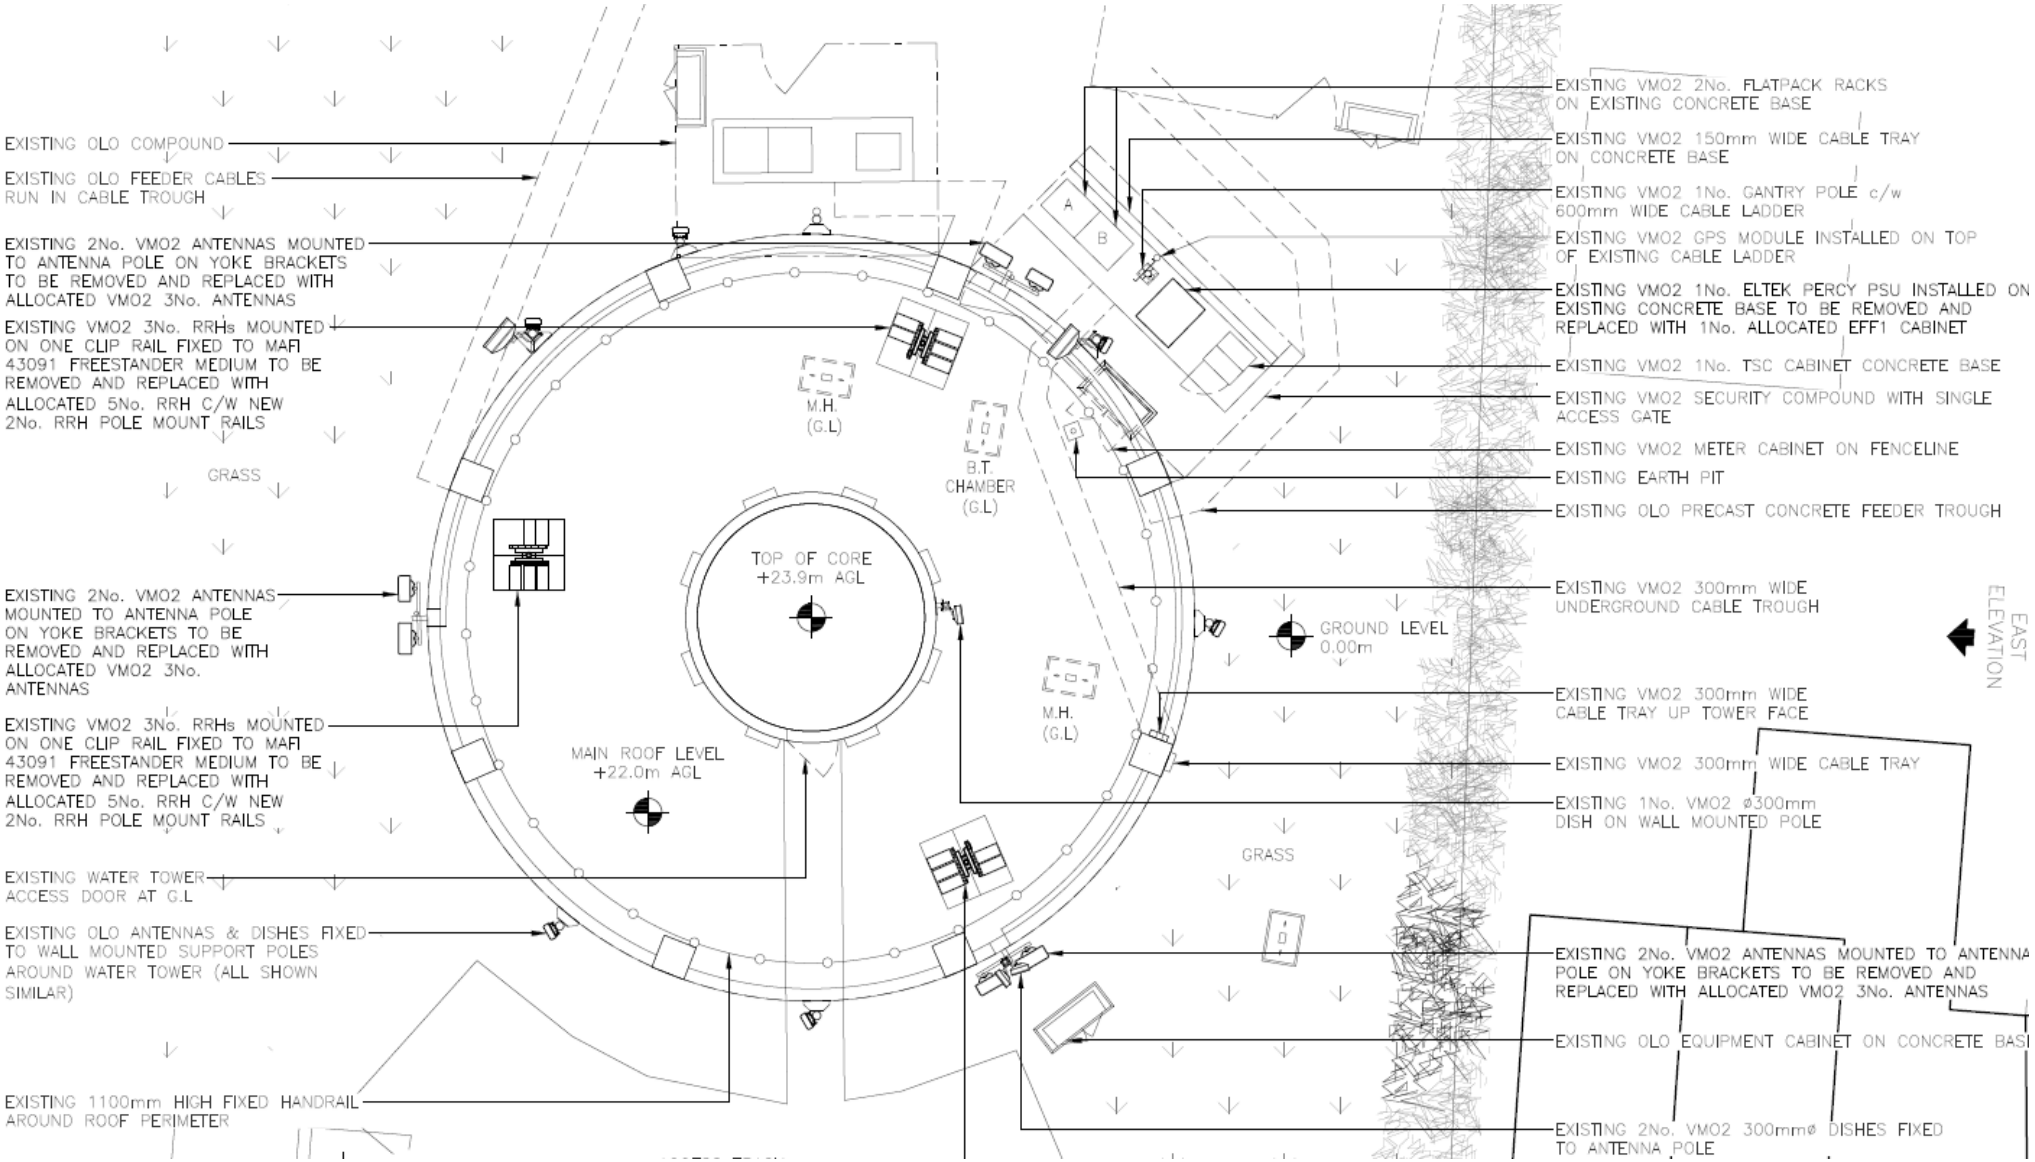
TASK	Roof scan
CLIENT	Jet NSL
PREPARED BY	Ayodele Fajuyigbe
SITE NAME	South Water Tower
DATE	22nd of October 2026

KA ENGINEERING GROUP

CHECKLIST	
Description	Actioned
Roof Scan Sector (All sectors)	
Plinth Scan Sector (All sectors)	
Beam Scan Sector (All sectors)	
Column Scan Sector (All sectors)	
Roof Support Layout (All sectors)	
Sketch of equipment position externally (All sectors)	
Roof Thickness (All sectors)	
Plant Room Wall Thickness	
Plant Room Brick Size	
Plant Room layout	
External photos of main building (4 faces)	
External main roof photos (All sectors)	
Internal photos (All sectors)	
External photographs of plant room (4 faces)	
Internal photos of plant room (4 faces)	
Load path photo	
Photo of survey equipment	

Notes


EXISTING OLO COMPOUND
EXISTING OLO FEEDER CABLES RUN IN CABLE TROUGH
EXISTING 2No. VMO2 ANTENNAS MOUNTED TO ANTENNA POLE ON YOKE BRACKETS TO BE REMOVED AND REPLACED WITH ALLOCATED VMO2 3No. ANTENNAS
EXISTING VMO2 3No. RRHs MOUNTED ON ONE CLIP RAIL FIXED TO MAFI 43091 FREESTANDER MEDIUM TO BE REMOVED AND REPLACED WITH ALLOCATED 5No. RRH C/W NEW 2No. RRH POLE MOUNT RAILS
GRASS
EXISTING 2No. VMO2 ANTENNAS MOUNTED TO ANTENNA POLE ON YOKE BRACKETS TO BE REMOVED AND REPLACED WITH ALLOCATED VMO2 3No. ANTENNAS
EXISTING VMO2 3No. RRHs MOUNTED ON ONE CLIP RAIL FIXED TO MAFI 43091 FREESTANDER MEDIUM TO BE REMOVED AND REPLACED WITH ALLOCATED 5No. RRH C/W NEW 2No. RRH POLE MOUNT RAILS
EXISTING WATER TOWER ACCESS DOOR AT G.L
EXISTING OLO ANTENNAS & DISHES FIXED TO WALL MOUNTED SUPPORT POLES AROUND WATER TOWER (ALL SHOWN SIMILAR)
EXISTING 1100mm HIGH FIXED HANDRAIL AROUND ROOF PERIMETER
M.H. (G.L)
B.T. CHAMBER (G.L)
TOP OF CORE +23.9m AGL
MAIN ROOF LEVEL +22.0m AGL
M.H. (G.L)
A
B
GROUND LEVEL 0.00m
GRASS
EXISTING VMO2 2No. FLATPACK RACKS ON EXISTING CONCRETE BASE
EXISTING VMO2 150mm WIDE CABLE TRAY ON CONCRETE BASE
EXISTING VMO2 1No. GANTRY POLE c/w 600mm WIDE CABLE LADDER
EXISTING VMO2 GPS MODULE INSTALLED ON TOP OF EXISTING CABLE LADDER
EXISTING VMO2 1No. ELTEK PERCY PSU INSTALLED ON EXISTING CONCRETE BASE TO BE REMOVED AND REPLACED WITH 1No. ALLOCATED EFF1 CABINET
EXISTING VMO2 1No. TSC CABINET CONCRETE BASE
EXISTING VMO2 SECURITY COMPOUND WITH SINGLE ACCESS GATE
EXISTING VMO2 METER CABINET ON FENCELINE
EXISTING EARTH PIT
EXISTING OLO PRECAST CONCRETE FEEDER TROUGH
EXISTING VMO2 300mm WIDE UNDERGROUND CABLE TROUGH
EXISTING VMO2 300mm WIDE CABLE TRAY UP TOWER FACE
EXISTING VMO2 300mm WIDE CABLE TRAY
EXISTING 1No. VMO2 ø300mm DISH ON WALL MOUNTED POLE
EXISTING 2No. VMO2 ANTENNAS MOUNTED TO ANTENNA POLE ON YOKE BRACKETS TO BE REMOVED AND REPLACED WITH ALLOCATED VMO2 3No. ANTENNAS
EXISTING OLO EQUIPMENT CABINET ON CONCRETE BASE
EXISTING 2No. VMO2 300mmø DISHES FIXED TO ANTENNA POLE
EAST ELEVATION

FROM ROOF EDGE TO CENTRE/MAIN CORE = 480cm

